

STATUS OF DISTRICT SECRETARIAT BUILDINGS AT DIFFERENT LOCATIONS **AS ON 30-09-2017** UNDER EASTERN ZONE



STATUS OF DISTRICT SECRETARIAT
BUILDINGS AT:
ROING
TEZU
NAMSAI
CHANGLANG
KHONSA

				P	UBLIC		RKS D				_	al figu	res in lakh	os) Anu	NORKS DESTANDANCE OF THE PROPERTY OF THE PROPE
S l. N o.	Name of Project	Sanctio n No. with Amount	Cumulati ve Funds released		cope of Work		Progres Achieveme 3/17	nt upto	Target 2		Achiev during 18 upt	2017- o 9/17	Cumula Achieveme 9/201	nt upto	UC Status/ Remark s
				Pr	ıy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	
	SPA	A 2012-13													
				Building	10100.55 sqm										UC Submitt ed:
		No.													500.00

	SPA	2012-13											
				Building	10100.55 sqm								UC Submitt
	Constant of	No. SPWD/											ed: 500.00
1	Constructi on of District Secretariat at Roing (PH-I)	PE- 07/SPA/ TC/201 3-14/61 Dtd.	500.00	Boundar y Wall	740 mtr	500.00	Compou nd wall in progress	62.00	100% of Block I		Compou nd wall in progress	62.00	Rs. 438.00 lakhs kept in Pt V.
	(= 32 3)	23/01/20 15											Land not availabl

Tender

Awarded

497.50

- Do -

497.5

-do-

SPA 2015-16

2

Phase II

No. SPWD/ PE-

26/SPA/

TC/201 4-15/718

Dtd.

17/11/20

15 for

Rs. 497.50 Lacs 497.50

-do-

held up.

UC:

497.00

Rs.

497.50

lakhs

kept in Pt-V

Tender

Awarded

497.5

0

PUBLIC WORKS DEPARTMENT

AP, ITANAGAR



Boundary wall in progress



Construction of District Secretariat at Roing in Lower Dibang Valley (Ph-I)

(Financial figures in lakhs

													/	ACHAL PRAD
SI · N	Name of Project	Sanction No. with Amount	Cumula tive Funds	Scope of	Work	Progres Achieveme 3/1/	ent upto	Target	2017-18	Achiev during i upto	2017-18	Cumula Achievemo 9/201	ent upto	UC Status/ Remark
0.		Amount	released	Phy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	S
	SPA 2	2012-13												
1	Construct ion of District Secretaria t at Tezu (PH-I) No. SPWD/ PE- 03/SPA/ TC/2013- 14/1484 Dtd. 04/02/2014		500.00	Building 9200.26 sqm	500.00	Block-A casting of slab for ground & 1st floor comp. column for 2nd	500.00	Block I 100%	300.00			Block-A casting of slab for ground & 1 st floor comp. column for 2 nd	500.00	UC submitt ed: 500.00
	(PH-I)	04/02/2014		Boundary wall 140.00 mtr										
	SPA 2	2015-16												
2	-Do-(PH- II)	No. SPWD/ PE- 25/SPA/ TC/2014- 15/641 Dtd. 02/11/2015 for Rs. 2500.00 Lacs	497.50	do	2500.00	- Do -	497.50	-do-				- Do -	497.50	UC Submitt ed: 497.50 Rs. 146.50 is kept in Part- V









PUBLIC WORKS DEPARTMENT (Financial figures in lakhs) AP, ITANAGAR

	WORKS DEAD
s)	The state of the s
-,	कर्मण्येवधिकारस्ते न
	A F
	ENAC SOL

														ACUA DRA
SI · N	Name of Project	Sanction No. with Amount	Cumulat ive Funds	Scope of V	Vork	Progre Achievem 3/1	ent upto	Target	t 2017- 8	Achiev during 2 upto	2017-18	Achie	ulative vement 9/2017	UC Status/ Remarks
0.			released	Phy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	
		SPA 2010-11												
1	C/O District Secretariat at Changlang Phase I	No. SPWD/ PE- 72/SPA/ JC/2010-11/912 Dtd. 09/12/2011 for Rs. 398.00 Lakhs	398.00		395.00	100%	398.00					100%	398.00	UC Rs. 398.00 lakhs
		SPA 2011-12												
2	Phase II	No. SPWD/ PE- 44/SPA/ JC/2012-13/929 Dtd. 25/12/2012 for Rs. 360.00 Lacs March/2015	360.00	First Block Office bldg: 3867 sq m Ret Wall 80 Mtr Compound Wall 170 Mtr	360.00	100%	360.00					100%	360.00	UC Rs. 360.00 lakhs
		SPA 2013-14												
3	Phase III	No. SPWD/ PE-63/SPA/ JC/2013-14/ 3566 Dtd. 05/12/2014 for Rs. 500.00 lakhs	497.50		500.00	100%	438.83					100%	438.83	UC Rs. 497.50 lakhs Rs. 58.67 in Part-V



SI · N	Name of Project	Sanction No. with Amount	Cumulat ive Funds	Scope of V	Vork	Progre Achievem 3/1	ent upto		t 2017- 8	Achiev during 2 upto	2017-18		ulative vement 9/2017	UC Status/ Remarks
0.	-		released	Phy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	
		SPA 2015-16 No. SPWD/ PE-												
4	Phase IV	No. SPWD/ PE- 23/SPA/ JC/2014-15/642 Dtd. 02/11/2015 for Rs. 500.00 Lacs	497.50	Second Block OfficeBuildin g 1509 Sq mtrs	500.00	Work in prog.	497.50	50%				Work in prog.	497.50	UC Rs. 497.50 Rs. 497.50 in Part-V
5	Phase-V	In process	556.00		1		ł	-1					ı	







C/o D.C. Office Complex / Mini Secretariate at Changlang District of Arunachal Pradesh (Ph:-I)





FIRST BLOCK DISTRICT SECRETARIAT AT CHANGLANG




(Financial figures in lakhs)

S l.	Name of	Sanction No.	Cumula tive Funds	Scope of	f Work	Progre Achievemo 3/1	ent upto	Target	2017-18	Achieve during 2 18 upto	2017-	Cumulat Achievemen 9/2017	t upto	Status of UC/ Remark
N o.	Project	with Amount	released	Phy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin	Phy.	Fin.	Remark s
	SF	PA 2012-13												
1	Constructi on of District Secretariat at Khonsa (PH-I)	No. SPWD/ PE-04/SPA/ JC/2013- 14/1821 Dtd. 25/03/2014 for Rs. 2500.00 lakhs	500.00	Office Building 8396.02 sqm	2500.00	1st Block	500.00	-				1 st Block	500.00	500.00
		SPA 2014-15	5			100%; 2 nd Block				2 nd Block 50%		100%; 2 nd Block		
2	Phase II	No. SPWD/ PE-24/SPA/ JC/2014- 15/719 Dtd. 17/11/2015 for Rs. 2500.00 lakhs	497.50	- Do -		20%	497.50	2 nd Block 100%	400.00	30 70		50%	497.50	497.50





DISTRICT SECRETARIAT AT KHONSA (BLOCK - C)





DISTRICT SECRETARIAT AT KHONSA (BLOCK - B)





DISTRICT SECRETARIAT AT KHONSA (2nd BLOCK)





DISTRICT SECRETARIAT AT KHONSA (3rd BLOCK)

PUBLIC WORKS DEPARTMENT

				•	ODLI	AP, I						ncial figures in	lakhs)	THAL PRAD
S I	Name of Projec	Sancti on No. with	Cumula tive Funds	Scope of W	ork	Progress Achievemen 3/17	nt upto	Targe	t 2017-18	durin	vement g 2017- to 9/17	Cumulative Achi upto 9/202		Status of UC/ Remar
N o	t	Amou nt	released	Phy.	Fin	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	ks
	SP.	A 2011-12												
1	Constru ction of District Secretar iat at Namsai (Ph-I)	No. SPWD / PE- 03/SP A/ TC/20 12- 13/900 Dtd. 19/12/2 012 for Rs. 450.00 lakhs March /2015	450.00	Office Building 8655 Sq mtr Boundary Wall 740 mtr	450.00	B/Wall- 630.00 Mtr, Block-A Bldg.100% compltd	947.50	100 %	500.00			B/Wall-630.00 Mtr, Block-A Bldg.100% compltd with	947.50	UC for Rs. 450.00 lakhs
		SPA	2015-16			with pinth area of						pinth area of 3800 sq mtr		
2	- Do -		497.50	- Do -	497.50	3800 sq mtr		100						UC for Rs. 497.50 lakhs

(PH-II) Rs. 73.54 lakhs kept in Part-V





Front view



C/o District Secretariat building at Namsai (First Block)





C/o District Secretariat building at Namsai (First Block)



STATUS OF DISTRICT CC ROAD AT DIFFERENT LOCATIONS **AS ON 30-09-2017** UNDER **EASTERN ZONE**



STATUS OF CC ROAD AT:

ROING
TEZU
CHANGLANG
KHONSA
LONGDING



(Financial figures in lakhs)

												`		, ,	
Sl. N	Name of Project	Sanction No. with Amount	Cumula tive Funds released	Scope	e of Wor	·k	Achieve	gressive ment upto 8/17	_	t 2017- 8	nt d 201	eveme uring 7-18 9/17	Achie	ulative vement 9/2017	UC Status/Re marks
				Phy.		Fin.	Phy.	Fin.	Phy.	Fin.	Phy	Fin.	Phy.	Fin.	
	SPA 2012-13														
	Construction of RCC road with	No. SPWD/ PE- 06/SPA/ TC/2013- 14/ 1622		CC Pavement with width 5.50 Mtr	5.02 Km									1000.0	UC Submitte d:
1	Drainage at Roing (PH-	Dtd. 04/03/201	1000.00	CC Drain	1.75 Km	1111.00	100%	1000.00	-	-			100%	0	1000.00 Work
	I)	4 for Rs. 1111.00 Lacs / March-		Slab culvert	18 Nos										Compltd









C/o RCC Road with drainage at Roing in Lower Dibang Valley District of Arunachal Pradesh under SPA-2012-13 (Ph-I)







C/o RCC Road with drainage at Roing in Lower Dibang Valley District of Arunachal Pradesh under SPA-2012-13 (Ph-I)

N 0.	Name of Project	Sanction No. with Amount	Cumulat ive Funds	Se			Progr	anning.						lakhs) 😘	
	PA 2011-12	Amount			Scope of Work		Achiever	ment upto	Tar: 2017		Achieve during 2 upto 9	2017-18	Achieve	mulative rement upto 0/2017	UC Status/Re marks
SP.	PA 2011-12		released	Ph	y.	Fin	Phy.	Fin.	Phy	Fin	Phy.	Fin.	Phy.	Fin.	liiai ks
				Widening	5.75 Km										
				Pavement	(3.75 m)										
				WBM-III	4.125 Km										
		No. SPWD/ PE-71/SPA/		DLCC	4.125 Km										
1 witl	C/o CC road with drainage at Khonsa (PH-I)	JC/2012- 13/331 Dtd. 09/03/2013	810.00	CC Pavement	4.125 Km	810.00	100%	810.00					100%	810.00	UC Submitte d for :
at		for Rs.	810.00	Pavement	(5.50 m)	810.00	100 %	810.00					100 %	810.00	810.00 Work
	(11-1)	810.00 Lacs / March-		WBM-III	3.20 Km										Compltd
		2015		DLCC	3.20 Km										
				CC Pavement	3.20 Km										
				Drain	4.20 Km										
SP.	PA 2012-13														
		No. SPWD/		Widening	1.66 Km										
		PE-05/SPA/ JC/2013-		S/Culvert	6 Nos										
		14/1626 Dtd.		G.S.B.	4.79 Km										
2 -D	Do-(PH-II)	25/02/2014 for Rs.	1000.00	CC Pavement	4.79 Km	1111.00	100%	1000.00					100%	1000.00	Work Compltd
		1111.00 Lacs /March- 2016		R&B Wall	210.00 m										







CC Pavement









Pucca Drain

Widening

CC Drain

RCC

S/Culvert

R&B Wall

CC

Pavement

Earth work

S/Culvert

Extn. Of

S/Culvert

R&B Wall

CC

Pavement

CC Drain

Cumula

tive

Funds

released

720.00

1000.00

Sanction

No. with

Amount

No. SPWD/

PE-

46/SPA/

JC/2012-

13/933

Dtd.

21/12/201

2 for Rs.

720.00

Lakhs /

March-2015

No.

SPWD/ PE-

03/SPA/

JC/2013-

14/1484

Dtd.

03/02/201

4 for Rs.

1111.00

Lacs

/March-2016

Sl.

No

1

2

Name of

Project

SPA 2011-12

C/o CC road

with drainage

at Changlang.

(Ph-I)

SPA 2012-13

-Do- (PH-II)

Phy.

Scope of Work

1.87 km

2.00 km

8 nos

850 mtr

2.18 km

1.71 km

4 nos

8 nos

470 mtr

1.96 km

1.90 km

PUBLIC WORKS DEPARTMENT AP. ITANAGAR

Fin

720.00

1111.00

Progressive

Achievement

upto 3/17

Fin.

720.00

925.04

Phy.

1.96

2.00

8

850

2.18

1.60

km

4 nos

6 nos

324.5

0 mtr

1.70

km

200

mtr

(Financial figures in lakhs)

Fin

Cumulative

Achievement

upto 9/2017

Fin.

720.00

925.04

Phy.

1.96

2.00

8

850

2.18

1.60

km

4 nos

6 nos

324.50

mtr

1.70

km

200

mtr

UC

Status/Re

marks

UC

Submitted

for:

720.00

Work

Compltd

UC

Submitted

for:

925.00

Rs. 74.95

lakhs kept

in Pt-V

Achievement

during 2017-

18 upto 9/17

Phy.


Target 2017-

18

Phy.

Fin



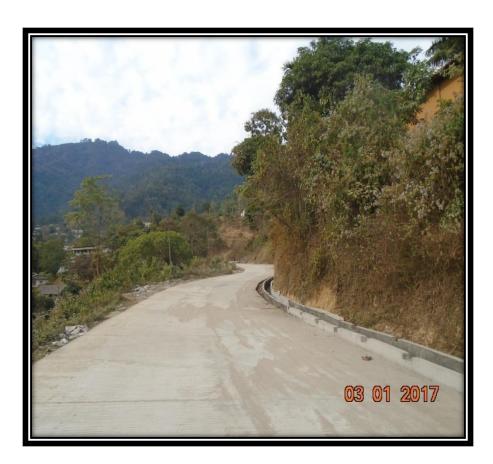



C/o C.C. Road with drainage at Changlang Length 3.00 km (Sub- F.C, Widening, Earth filling, Cross Drainage, Protection work, Concrete pavement and C.C. Drain) (Ph:-I)

F	PUBLIC							aial f		aa in I	alth a	WORKS DEATH
		AP, I	TAN/	AGA	R		(Finan	ciai ji	gure	25 IN 1	akns)	T S
ılati ınds sed	Scop	e of Work		Achie	gressive evement to 3/17	Target 1		Achie en duri 2017 upto	t ing '-18	Ach	mulative ievement o 9/2017	UC Status/ Remarks
	Phy.		Fin	Phy.	Fin.	Phy.	Fin.	Phy .	Fi n.	Phy ·	Fin.	

3.25

3.25

3.25

3.89

2

385

400

2.22

1

2

1

10

400

1000.00

497.50

UC:

1000.00

Work

complete

d

UC

Submitte

d: 497.50

Work

Compltd

	PUBLIC WORKS DEPARTMENT												
AP, ITANAGAR (Financial figures in lakhs)											akhs)	कर्मण्येवधिकारस्ते	
ılati ınds sed	Scope of Work			Progressive Achievement upto 3/17		Target 2017- 18		Achievem ent during 2017-18 upto 9/17		Cumulative Achievement upto 9/2017		UC Status Remarl	
	Phy. Fin		Fin	Phy.	Fin.	Phy.	Fin.	Phy .	Fi n.	Phy •	Fin.		
	Widening	3.22 Km		3.25						3.25			

1000.00

497.50

1200

	PUBLIC WORKS DEPARTIVIENT														WORKS DEADAR	
AP, ITANAGAR (Financial figures in lakhs)													akhs) 🥞	कर्मण्येवधिकारस्ते सु		
Sl. No.\	Name of Project	Sanction No. with Amount	Cumulati ve Funds released	Scope of Work			Progressive Achievement upto 3/17		Target 2017- 18		Achievem ent during 2017-18 upto 9/17		Cumulative Achievement upto 9/2017		UC Status/ Remarks	
				Phy.		Fin	Phy.	Fin.	Phy.	Fin.	Phy	Fi n.	Phy	Fin.		
				Widening	3.22 Km		3.25						3.25			

1111.00

497.50

3.25

3.25

3.25

3.89

2

385

2.22

1

2

1

10

														()	
SI. No.\	Name of Project	Sanction No. with Amount	Cumulati ve Funds released	Scope of Work			Progressive Achievement upto 3/17		Target 2017- 18		Achievem ent during 2017-18 upto 9/17		Cumulative Achievement upto 9/2017		UC Status Remarl
				Phy.		Fin	Phy.	Fin.	Phy.	Fin.	Phy .	Fi n.	Phy ·	Fin.	
				Widening	3.22 Km		3.25						3.25		

5.35 Km

5.35 Km

5.35 Km

3.89 Km

2 Nos

320 Mtr

1600

Mtr

2.22 Km

1 No

2 Nos

1 No

10 Nos

G.S.B.

DLCC

CC Pavement

CC Drain

S/Culvert 6

mtr **R&B Wall**

Steel railing

DLCC

Pavement RCC S/Cul 1m

Widening of

existing S/Cul

@ 2 m on both

side

Widening of

existing S/Cul

@ 1.5 m on both side

Widening of

junction/curve

No. SPWD/

PE-08/SPA/

JC/2013-

14/1496 Dtd.

06/02/2014 for

Rs. 1111.00

Lakhs /

No. SPWD/

PE-67/SPA/

JC/2013-

14/2360 Dtd.

28/10/2014 for

Rs. 497.50

Lakhs

1000.00

497.50

C/o RCC road

with drainage

at Longding

(**PH-I**)

C/o RCC road

Tezu

Township

1

2












Construction of C.C. Road in Tezu Township



CC Road with drainage at Longding



Circuit House Tinali



Circuit House Road



Approach Road to Longding Sub- Division.



Circuit House Road





HELIPAD ROAD



HELIPAD ROAD



CRPF TINALI



SP BUNGLOW ROAD

CC Road with drainage at Longding



SSB turning



AMBEDKAR ROAD



LB ROAD TINALI/ DC OFFICE TINALI



DC BUNGLAW TINALI





General ground road



SSB COLONY ROAD

CC Road with drainage at Longding







GENERAL GROUND ROAD

CC Road with drainage at Longding
